


FY 19-20 BRIDGE PROJECTS LETTING LIST (PER PS 7/11/2019)

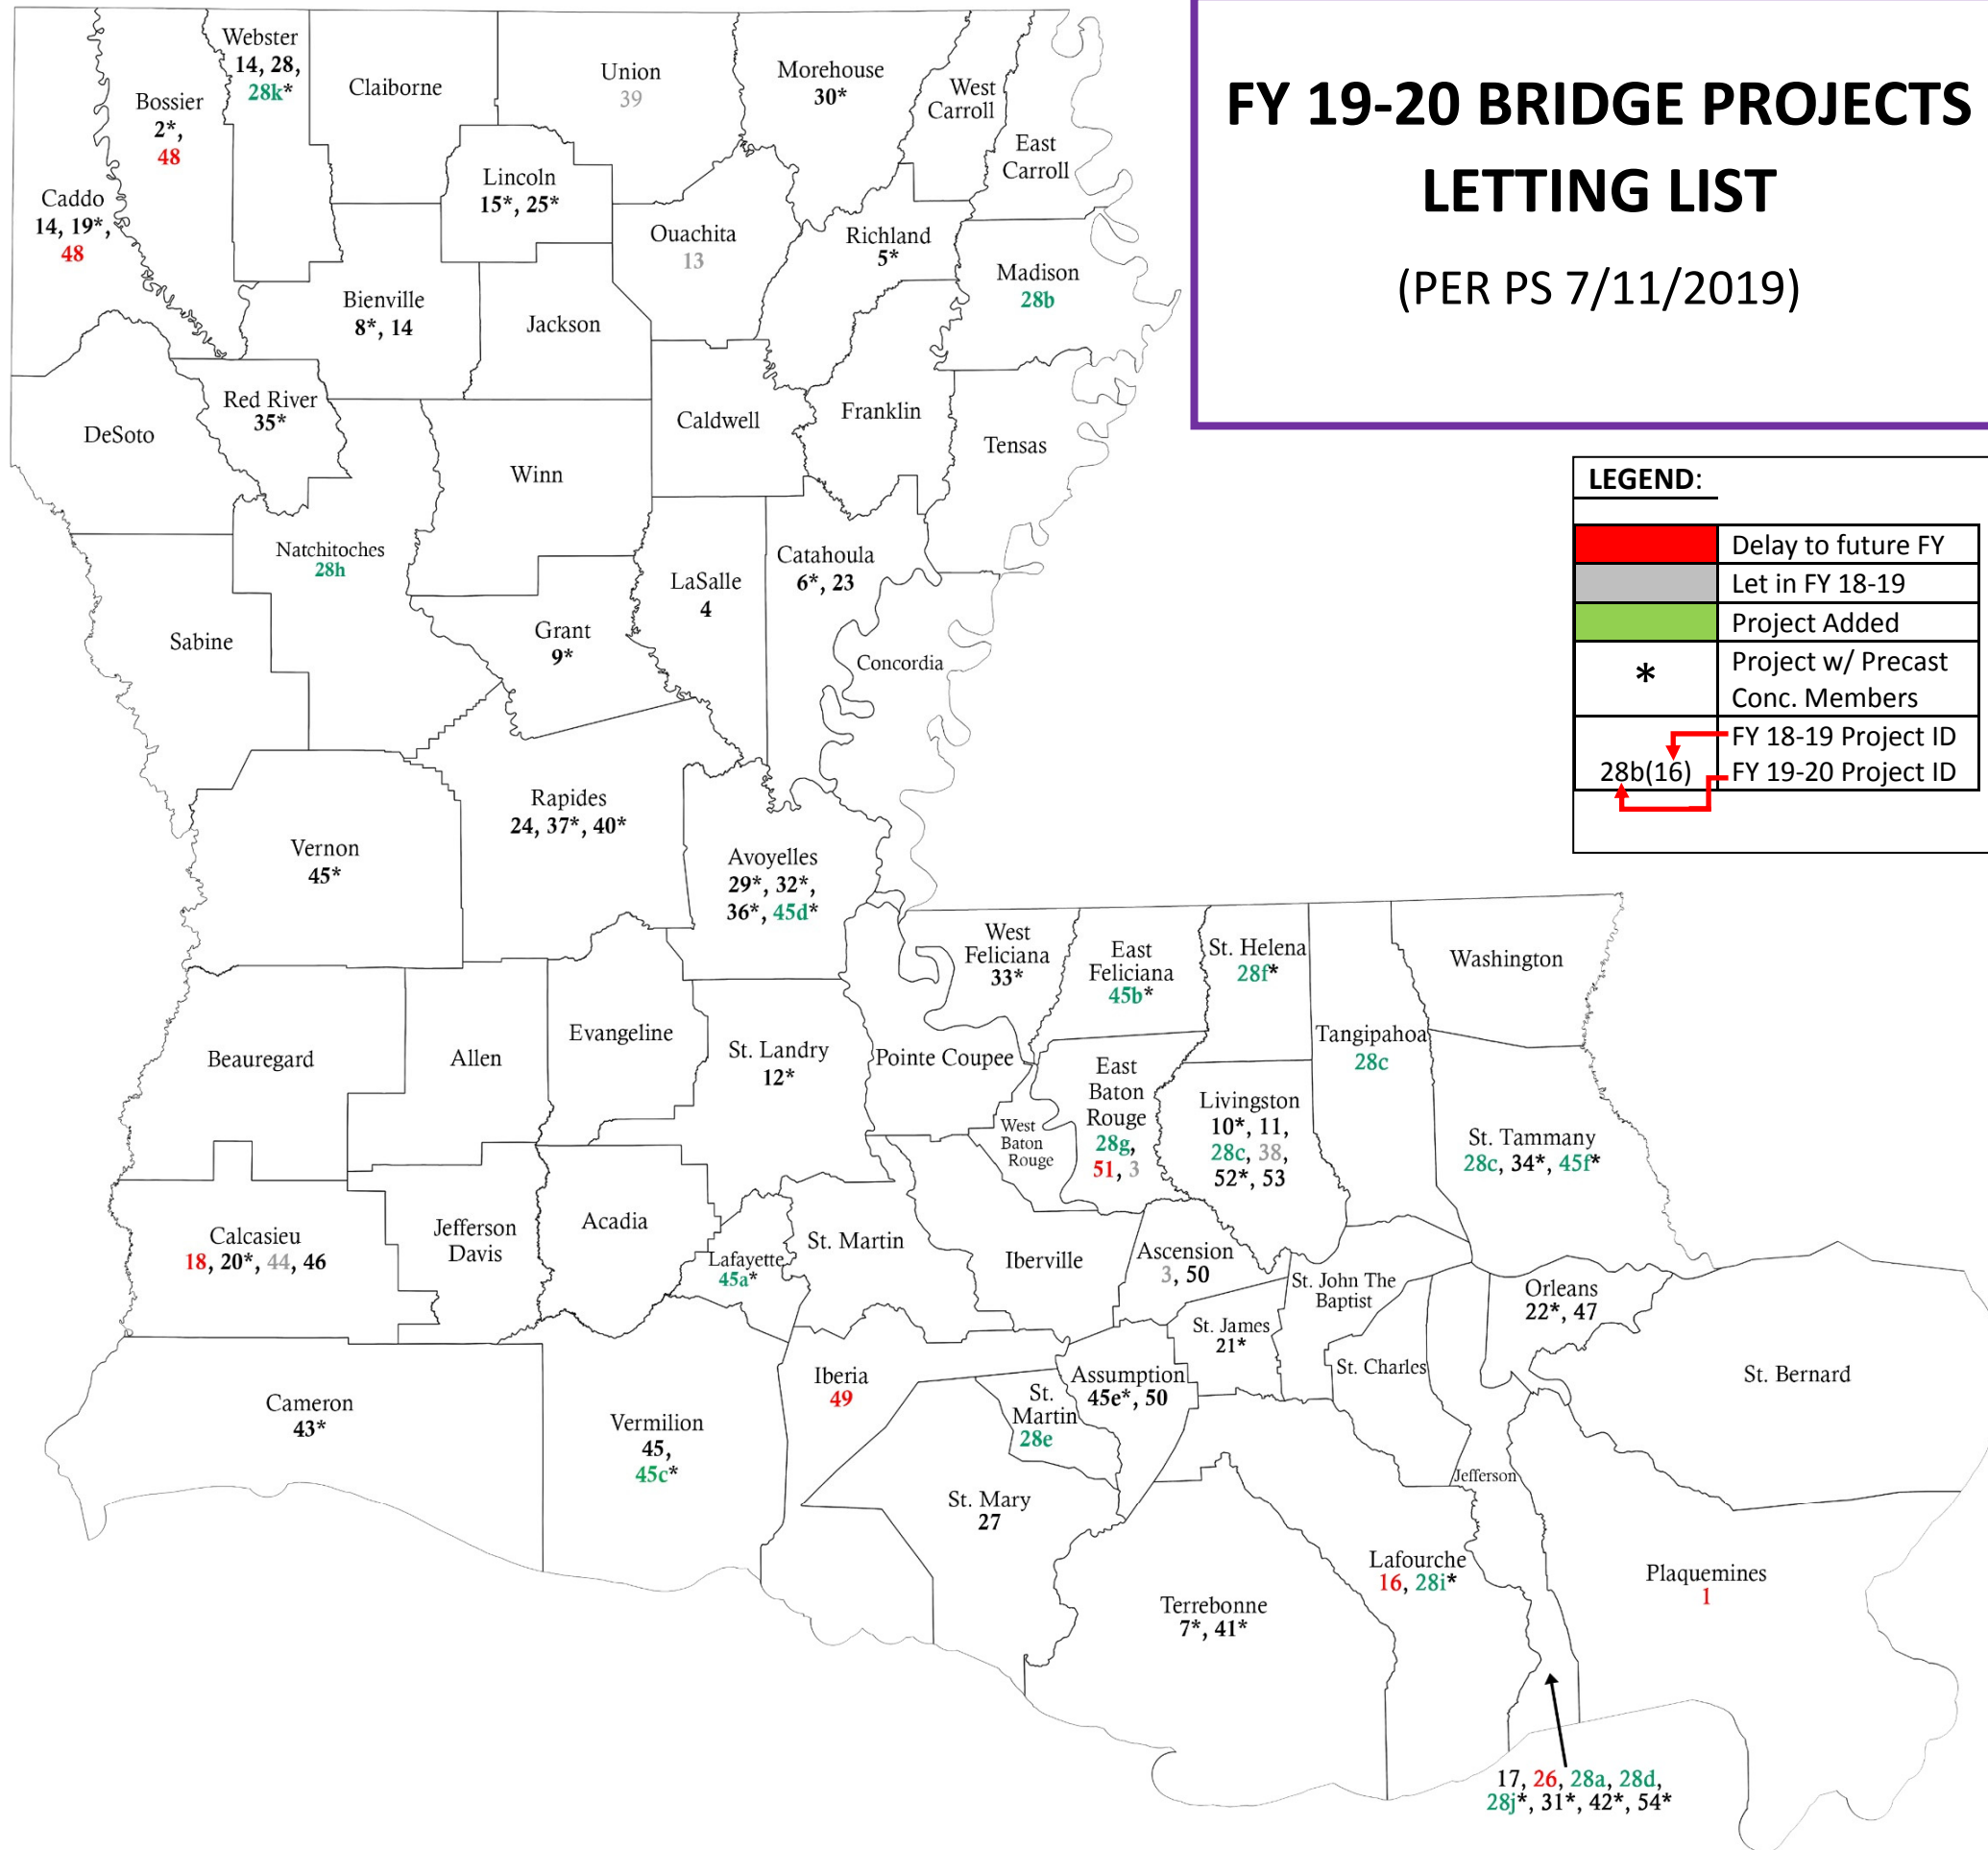

LEGEND:

	Delay to future FY
	Let in FY 18-19
	Project Added
*	Project w/ Precast Conc. Members
28b(16)	FY 18-19 Project ID
17, 26, 28a, 28d, 28j, 31, 42, 54	FY 19-20 Project ID

Main Category	Project ID	Project No.	Letting Date	New Letting Date
On-System Bridge Program	1	H.004791	7/3/2019	XX
	2	* H.000118	7/10/2019	
	3	H.000337	7/10/2019	Let 18/19 FY
	4	H.000754	7/10/2019	12/11/2019
	5	* H.000974	7/10/2019	9/11/2019
	6	* H.001140	7/10/2019	9/11/2019
	7	* H.001498	7/10/2019	8/14/2019
	8	* H.001537	7/10/2019	11/13/2019
	9	* H.001842	7/10/2019	7/24/2019
	10	* H.002375	7/10/2019	9/11/2019
	11	H.002381	7/10/2019	3/11/2020
	12	* H.008332	7/10/2019	11/13/2019
	13	H.010012	7/10/2019	Let 18/19 FY
	14	H.012451	12/12/2018	
	15	* H.001679	8/14/2019	9/11/2019
	16	H.002794	8/14/2019	10/14/2020
	17	H.013706	8/14/2019	12/11/2019
	18	H.010000	5/13/2020	9/9/2020
	19	* H.001661	10/9/2019	3/11/2020
	20	* H.003184	11/13/2019	
	21	* H.009481	12/11/2019	
	22	* H.010018	12/11/2019	
	23	H.013273	12/11/2019	
	24	H.000577	1/8/2020	
	25	* H.000133	2/12/2020	
	26	H.002264	3/11/2020	7/13/2020
	27	H.011487	3/11/2020	
	28	H.001799	5/13/2020	
	28a	H.013840		7/24/2019
	28b (16)	H.012739		7/24/2019
	28c (11)	H.012650		7/24/2019
	28d	H.013839		8/14/2019
	28e (26)	H.011485		9/11/2019
	28f (23)	* H.008312		10/9/2019
	28g (15)	H.012469		12/11/2019
	28h	H.013832		5/13/2020
	28i (28)	* H.008118		6/10/2020
	28j	* H.013842		6/10/2020
	28k (21)	* H.010008		8/14/2019
	29	* H.006016	7/10/2019	9/11/2019
	30	* H.006170	7/10/2019	12/11/2019
	31	* H.010626	7/10/2019	1/8/2020
	32	* H.011523	7/10/2019	10/9/2019
	33	* H.010597	8/14/2019	12/11/2019
	34	* H.010668	2/12/2020	2/12/2020
	35	* H.011087	2/12/2020	2/12/2020
	36	* H.011524	2/12/2020	2/13/2020
	37	* H.011526	2/12/2020	5/12/2021
	38	H.011528	2/12/2020	Let 18/19 FY
	39	H.011530	2/12/2020	Let 18/19 FY
	40	* H.011531	2/12/2020	2/12/2020
	41	* H.011533	2/12/2020	2/13/2020
	42	* H.011534	2/12/2020	2/14/2020
	43	* H.011545	2/12/2020	2/15/2020
44	H.011546	2/12/2020	Let 18/19 FY	
45	* H.006339	6/10/2020	6/10/2020	
45a (42)	* H.010557		3/11/2020	
45b (43)	* H.010562		12/11/2019	
45c (35)	* H.010867		12/11/2019	
45d (36)	* H.011522		11/13/2019	
45e	* H.011767		2/12/2020	
45f (45)	* H.011921		10/9/2019	
46	H.005967	3/11/2020	3/11/2020	
47	H.013442	8/14/2019	8/14/2019	
48	H.012889	1/8/2020	7/8/2020	
49	H.010155	7/10/2019	3/10/2021	
50	H.011767	7/10/2019	2/12/2020	
51	H.011791	7/10/2019	8/11/2021	
52	* H.011828	7/10/2019	4/8/2020	
53	H.013158	11/13/2019	11/13/2019	
54	* H.007208	1/8/2020	1/8/2020	

Summary of Quantities

Estimated Bridge Quantities FY 19-20	REINFORCING STEEL IN POUNDS	STRUCTURAL METALWORK IN POUNDS	QUAD BEAM LN FT	TYPE II LN FT	TYPE III LN FT	TYPE IV LN FT	TYPE BT72 LN FT	TYPE BT78 LN FT	LG-25	LG-36	LG-45	LG-54	LG-63	LG-72	LG-78	U BEAM	PILES 12" LN FT	PILES 14" LN FT	PILES 16" LN FT	PILES 18" LN FT	PILES 24" LN FT	PILES 30" LN FT	PILES 36" LN FT	PILES 54" LN FT	DRILLED SHAFT LN FT	STEEL PILES LN FT	STEEL SHEET PILING SQFT	TX-62 GIRDER	TX-70 GIRDER
		9,529,592	4,874,875	8,731	892	0	0	0	0	0	5,820	8,055	5,076	12,376	0	0	0	4,200	12,230	63,715	68,183	93,329	26,921	5,151	0	3,982	835	101,209	0

LEGEND:

	Delay to future FY
	Let in FY 18-19
	Project Added
*	Project w/ Precast Conc. Members
	FY 18-19 Project ID
28b(16)	FY 19-20 Project ID
